


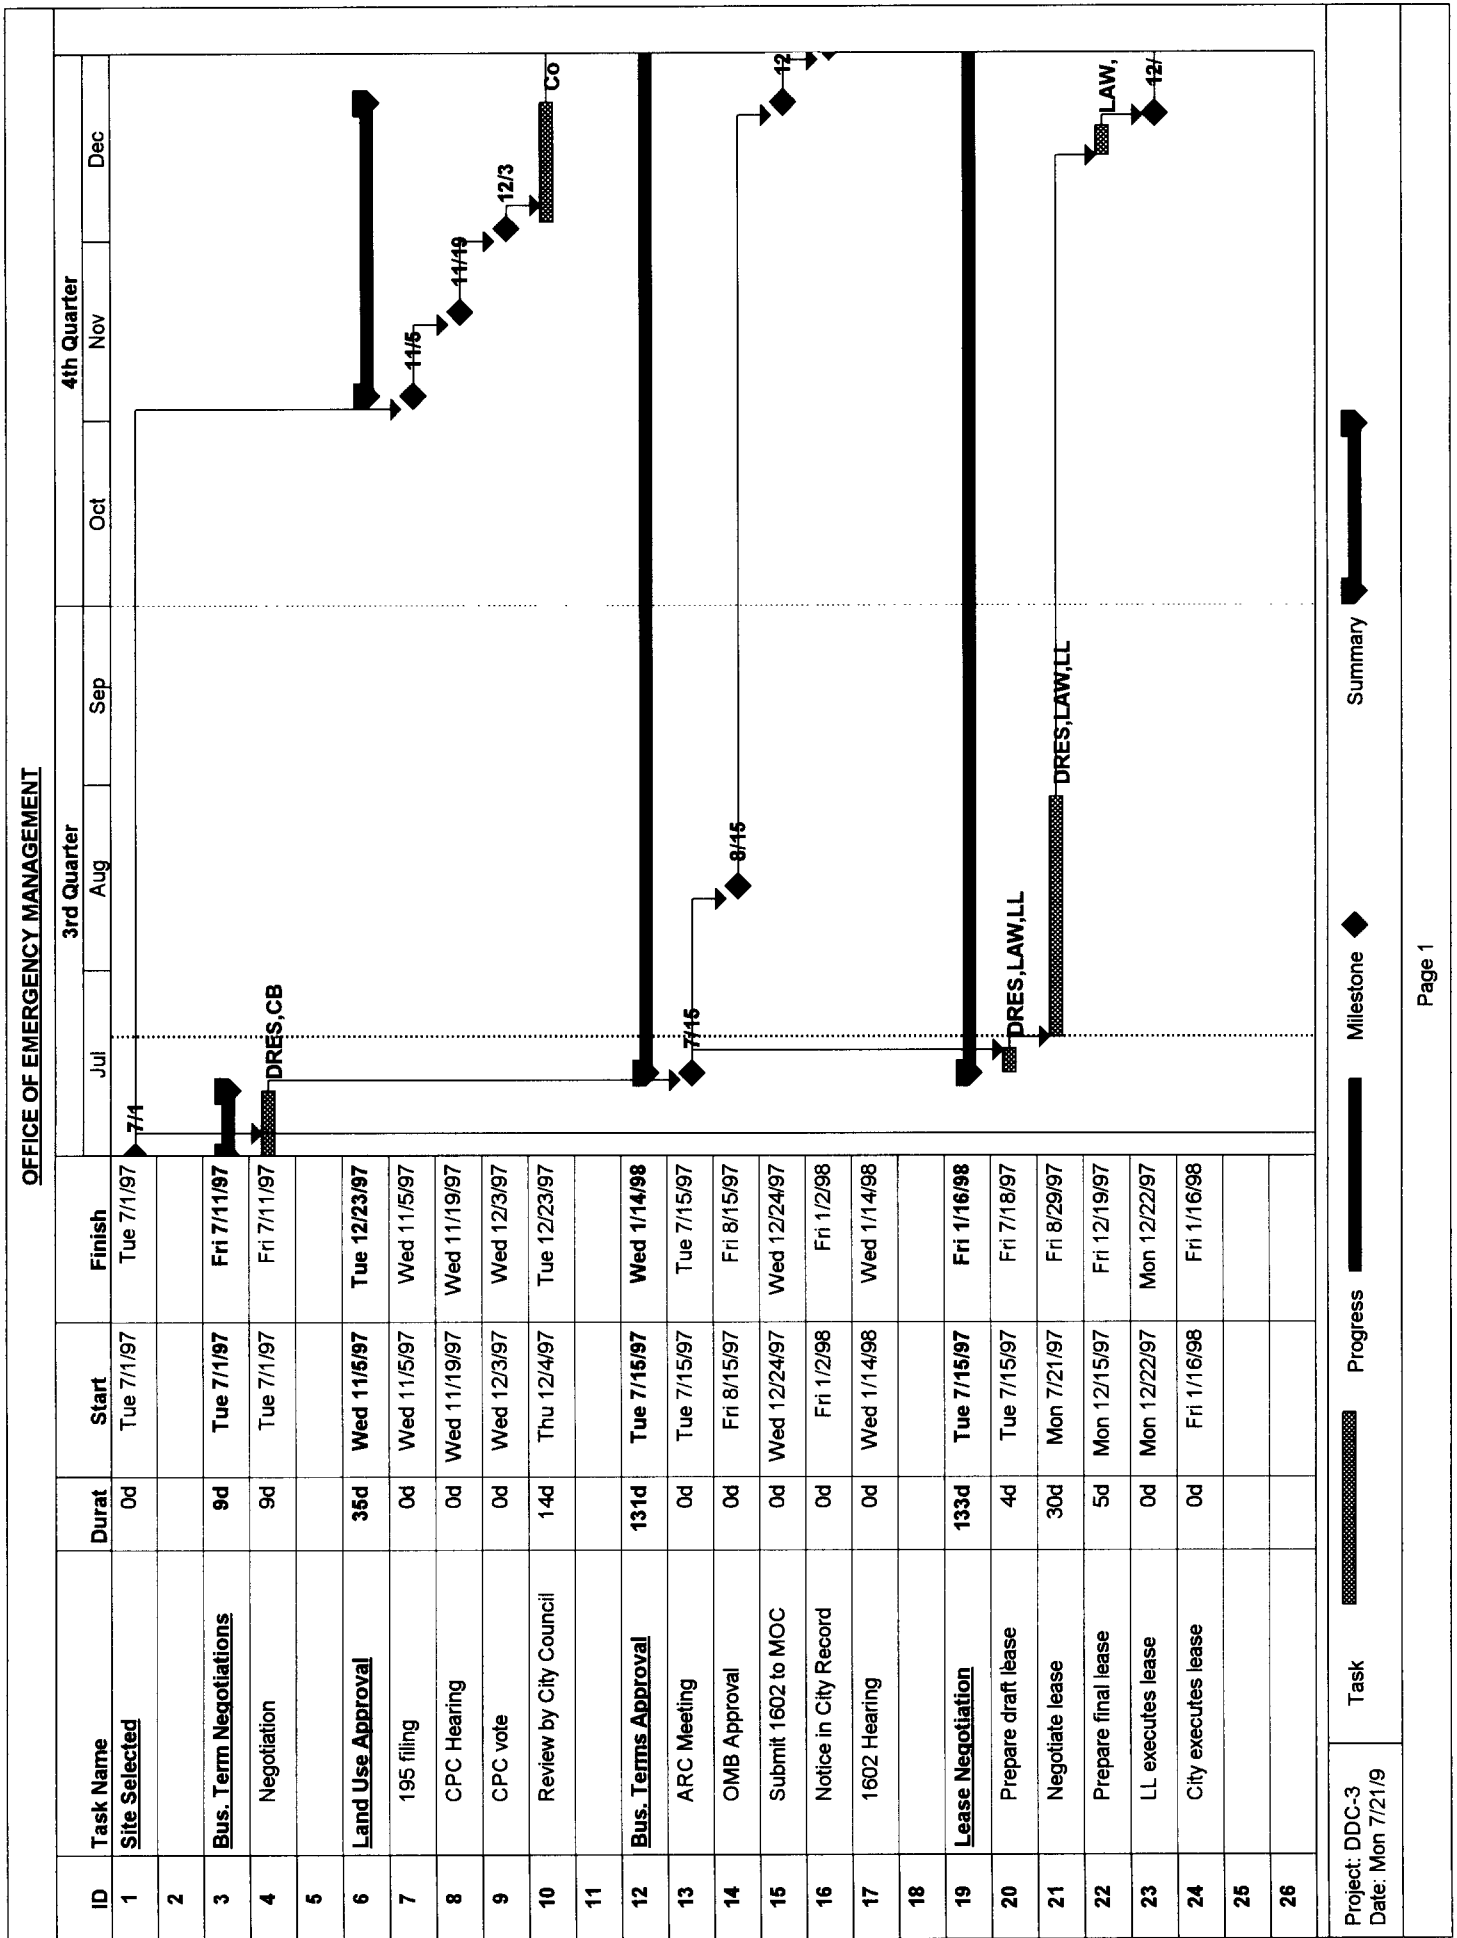

OFFICE OF EMERGENCY MANAGEMENT

		3rd Quarter			4th Quarter		
		Jul	Aug	Sep	Oct	Nov	Dec
ID	Task Name	Durat	Start	Finish			
27	Prelim. Plans	74d	Tue 7/1/97	Fri 10/10/97			
28	Revise P&E	19d	Tue 7/1/97	Fri 7/25/97			
29	Engage Arch.	10d	Mon 7/28/97	Fri 8/8/97			
30	Prepare prelim. plans	25d	Mon 8/11/97	Fri 9/12/97			
31	Review & Revisions	20d	Mon 9/15/97	Fri 10/10/97			
32	OEM sign-off plans	0d	Fri 10/10/97	Fri 10/10/97			
33							
34	Final Plans	55d	Mon 10/13/97	Fri 12/26/97			
35	Construction Docs.	35d	Mon 10/13/97	Fri 11/28/97			
36	Review & Revisions	20d	Mon 12/1/97	Fri 12/26/97			
37	Final plans sign-off	0d	Fri 12/26/97	Fri 12/26/97			
38							
39	Construction	120d	Mon 12/29/97	Fri 6/12/98			
40	Bids	20d	Mon 12/29/97	Fri 1/23/98			
41	Bids approved	0d	Fri 1/23/98	Fri 1/23/98			
42	Permits	5d	Mon 1/26/98	Fri 1/30/98			
43							
44	Construction - Office	40d	Mon 2/2/98	Fri 3/27/98			
45	Sub. Comp.	0d	Fri 3/27/98	Fri 3/27/98			
46	Furniture & Phones	10d	Mon 3/30/98	Fri 4/10/98			
47	Occupancy - Office	0d	Fri 4/10/98	Fri 4/10/98			
48							
49	Construction - Tech	80d	Mon 2/2/98	Fri 5/22/98			
50	Sub. Comp.	0d	Fri 5/22/98	Fri 5/22/98			
51	Furniture, Phones, Equip.	15d	Mon 5/25/98	Fri 6/12/98			
52	Occupancy	0d	Fri 6/12/98	Fri 6/12/98			

Project: DDC-3
Date: Mon 7/21/9

Task

Progress

Milestone

Summary

