


Date: November 14, 1997; Updated 05/21/98



Mayor's Office of Emergency Management
7 World Trade Center

Date: November 14, 1997; Updated 02/02/98

Excl. 03-16-98

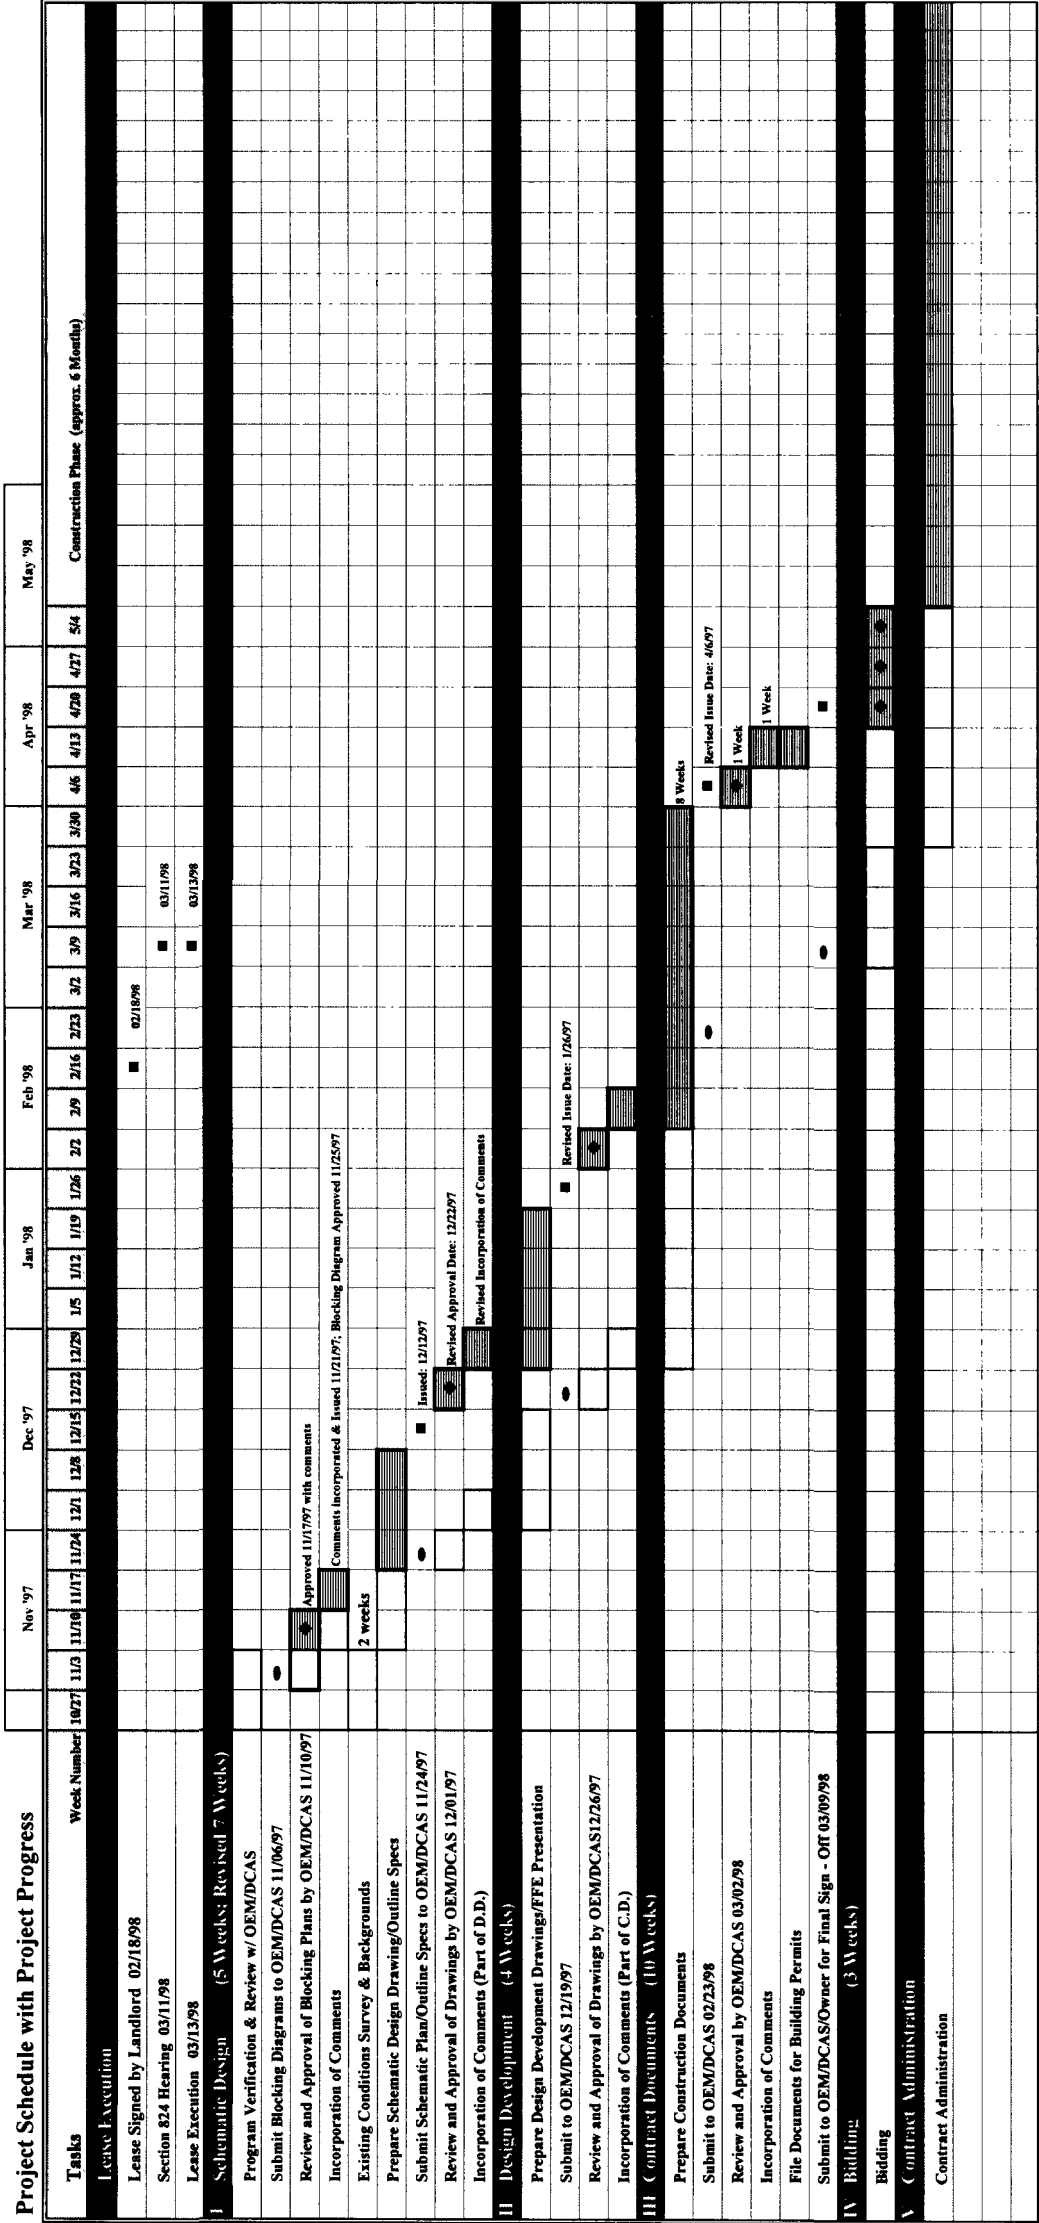

Legend

Proposed Project Schedule 11/14/97

Proposed Submission Date

Proposed Review & Approval


Actual/Projected Schedule Revision (as of 12/03/97)

Actual/Projected Submission Date

Actual/Projected Review & Approval

Mayor's Office of Emergency Management
7 World Trade Center

Date: November 14, 1997; Updated 05/21/98

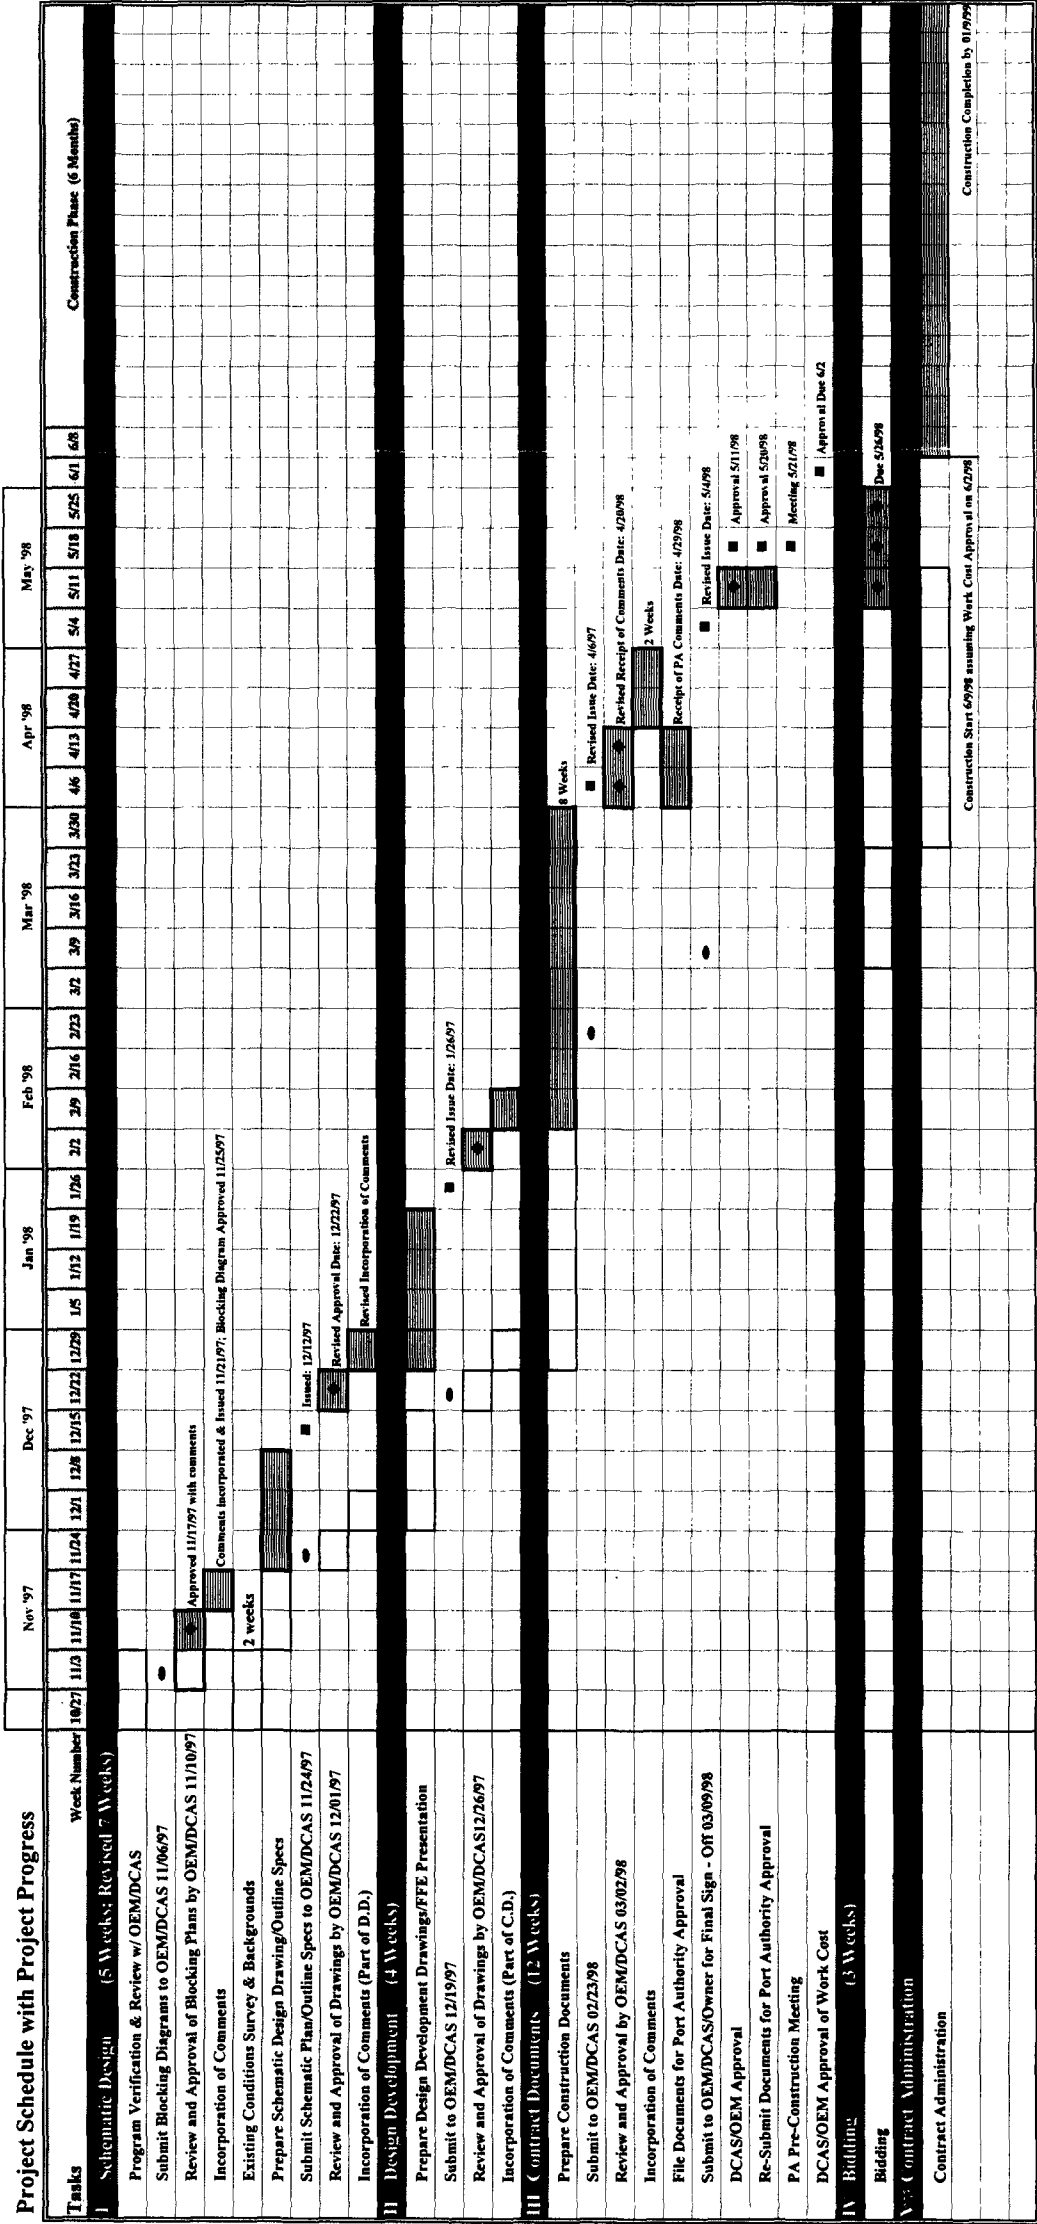

SWANKE HAYDEN CONNELL ARCHITECTS

Mayor's Office of Emergency Management
7 World Trade Center

Date: November 11, 1997

Proposed Project Schedule

Proposed Project Schedule																									
Tasks	Week Number	Nov '97		Dec '97		Jan '98		Feb '98		Mar '98		Apr '98	May '98	Construction Phase (approx. 6 Months)											
		10/27	11/3	11/10	11/17	11/24	12/1	12/8	12/15	12/22	12/29	1/5	1/12		1/19	1/26	2/2	2/9	2/16	2/23	3/2	3/9	3/16	3/23	3/30
I Schematic Design (5 Weeks)																									
Program Verification & Review w/ OEM/DCAS																									
Submit Blocking Diagrams to OEM/DCAS 11/06/97																									
Review and Approval of Blocking Plans by OEM/DCAS 11/10/97																									
Incorporation of Comments																									
Existing Conditions Survey & Backgrounds																									
Prepare Schematic Design Drawing/Outline Specs																									
Submit Schematic Plan/Outline Specs to OEM/DCAS 11/24/97																									
Review and Approval of Drawings by OEM/DCAS 12/01/97																									
Incorporation of Comments (Part of D.D.)																									
II Design Development (4 Weeks)																									
Prepare Design Development Drawings/FFE Presentation																									
Submit to OEM/DCAS 12/19/97																									
Review and Approval of Drawings by OEM/DCAS 12/26/97																									
Incorporation of Comments (Part of C.D.)																									
III Contract Documents (11 Weeks)																									
Prepare Construction Documents																									
Submit to OEM/DCAS 02/23/98																									
Review and Approval by OEM/DCAS 03/02/98																									
Incorporation of Comments																									
File Documents for Building Permits																									
Submit to OEM/DCAS/Owner for Final Sign - Off 03/16/98																									
IV Bidding (4 Weeks)																									
Bidding																									
V Contract Administration																									
Contract Administration																									

SWANKE HAYDEN CONNELL ARCHITECTS

Mayor's Office of Emergency Management
7 World Trade Center

Date: November 14, 1997; Updated 02/02/98

Project Schedule with Project Progress

