


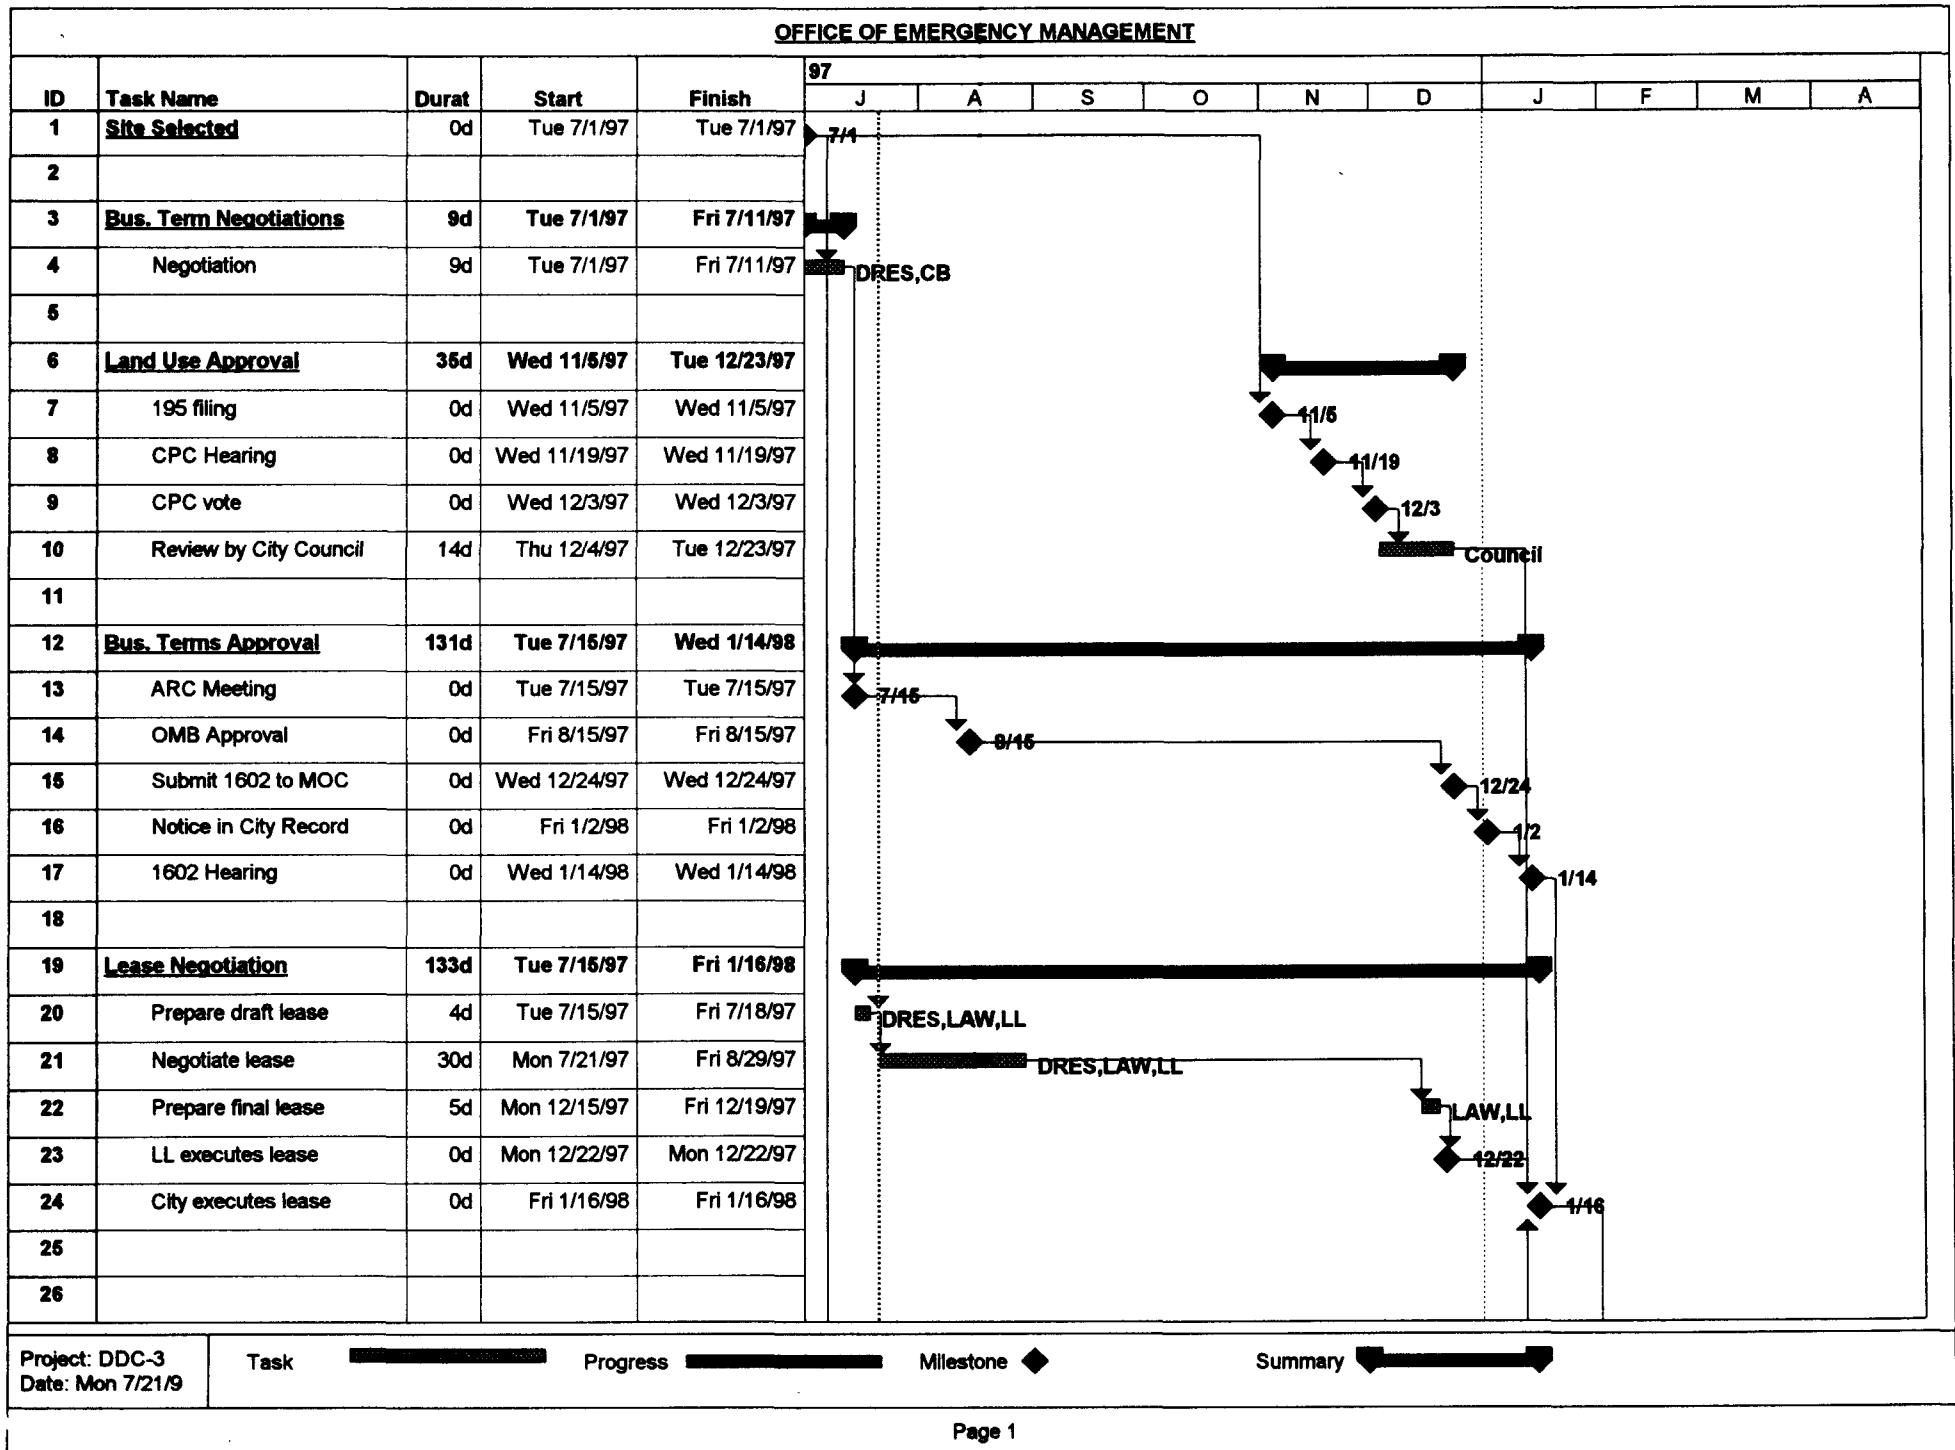

OFFICE OF EMERGENCY MANAGEMENT

ID	Task Name	Durat	Start	Finish	J	A	S	O	N	D	J	F	M	A
27	Prelim. Plans	74d	Tue 7/1/97	Fri 10/10/97										
28	Revise P&E	19d	Tue 7/1/97	Fri 7/25/97										
29	Engage Arch.	10d	Mon 7/28/97	Fri 8/8/97										
30	Prepare prelim. plans	25d	Mon 8/11/97	Fri 9/12/97										
31	Review & Revisions	20d	Mon 9/15/97	Fri 10/10/97										
32	OEM sign-off plans	0d	Fri 10/10/97	Fri 10/10/97										
33														
34	Final Plans	66d	Mon 10/13/97	Fri 12/26/97										
35	Construction Docs.	35d	Mon 10/13/97	Fri 11/28/97										
36	Review & Revisions	20d	Mon 12/1/97	Fri 12/26/97										
37	Final plans sign-off	0d	Fri 12/26/97	Fri 12/26/97										
38														
39	Construction	120d	Mon 12/29/97	Fri 6/12/98										
40	Bids	20d	Mon 12/29/97	Fri 1/23/98										
41	Bids approved	0d	Fri 1/23/98	Fri 1/23/98										
42	Permits	5d	Mon 1/26/98	Fri 1/30/98										
43														
44	Construction - Office	40d	Mon 2/2/98	Fri 3/27/98										
45	Sub. Comp.	0d	Fri 3/27/98	Fri 3/27/98										
46	Furniture & Phones	10d	Mon 3/30/98	Fri 4/10/98										
47	Occupancy - Office	0d	Fri 4/10/98	Fri 4/10/98										
48														
49	Construction - Tech	80d	Mon 2/2/98	Fri 5/22/98										
50	Sub.Comp.	0d	Fri 5/22/98	Fri 5/22/98										
51	Furniture, Phones, Equip.	15d	Mon 5/25/98	Fri 6/12/98										
52	Occupancy	0d	Fri 6/12/98	Fri 6/12/98										

Project: DDC-3
Date: Mon 7/21/9

Task

Progress

Milestone

Summary

