


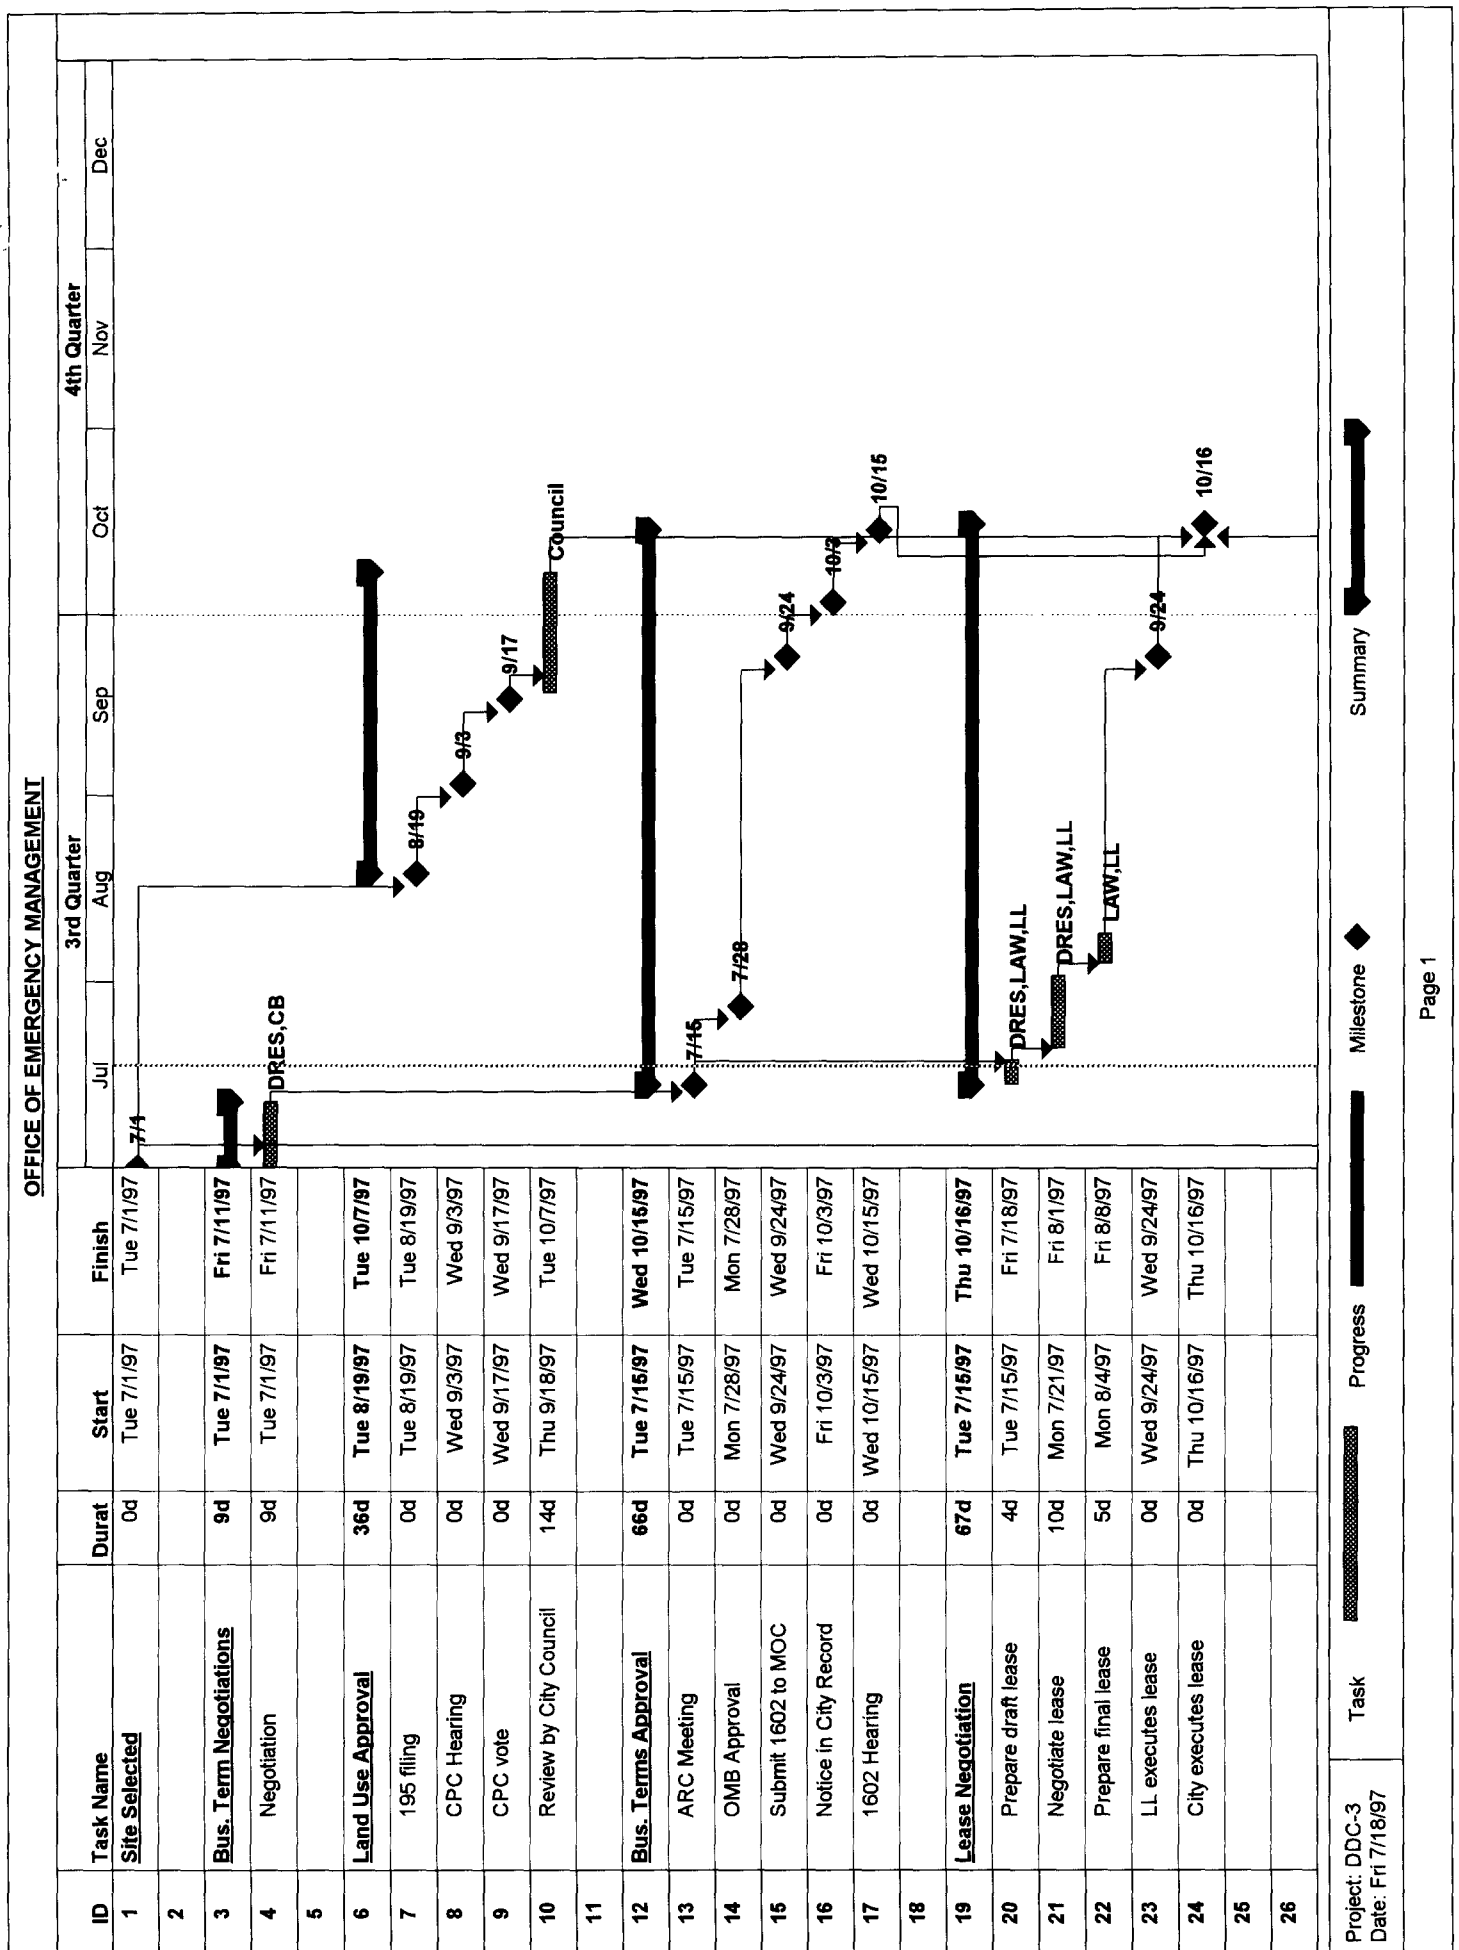

OFFICE OF EMERGENCY MANAGEMENT

ID	Task Name	Durat	Start	Finish	3rd Quarter				4th Quarter			
					Jul	Aug	Sep	Oct	Nov	Dec		
27	<u>Prelim. Plans</u>	49d	Tue 7/1/97	Mon 9/8/97								
28	Revise P&E	10d	Tue 7/1/97	Mon 7/14/97								
29	Engage Arch.	14d	Tue 7/15/97	Fri 8/1/97								
30	Prepare prelim. plans	15d	Mon 8/4/97	Fri 8/22/97								
31	Review by DRES & OEM	5d	Mon 8/25/97	Fri 8/29/97								
32	Revise Plans	5d	Mon 9/1/97	Fri 9/5/97								
33	OEM sign-off plans	0d	Mon 9/8/97	Mon 9/8/97								
34												
35	<u>Final Plans</u>	45d	Mon 9/8/97	Mon 11/10/97								
36	Construction Docs.	35d	Mon 9/8/97	Fri 10/24/97								
37	Review Plans	5d	Mon 10/27/97	Fri 10/31/97								
38	Revise Plans	5d	Mon 11/3/97	Fri 11/7/97								
39	Final plans sign-off	0d	Mon 11/10/97	Mon 11/10/97								
40												
41	<u>Construction</u>	104d	Tue 11/11/97	Fri 4/3/98								
42	Bids	14d	Tue 11/11/97	Fri 11/28/97								
43	Bids apporved	0d	Fri 11/28/97	Fri 11/28/97								
44	Construction - Office	40d	Mon 12/1/97	Fri 1/23/98								
45	Sub. Comp.	0d	Fri 1/23/98	Fri 1/23/98								
46	Furniture & Phones	10d	Mon 1/26/98	Fri 2/6/98								
47	Occupancy - Office	0d	Fri 2/6/98	Fri 2/6/98								
48	Construction - Tech	80d	Mon 12/1/97	Fri 3/20/98								
49	Sub.Comp.	0d	Fri 3/20/98	Fri 3/20/98								
50	Furniture & Phones	10d	Mon 3/23/98	Fri 4/3/98								
51	Occupancy	0d	Fri 4/3/98	Fri 4/3/98								

Project: DDC-3
Date: Fri 7/18/97

Task

Progress

Milestone

Summary

