

01/03/1995 06:59 2129499762

AMBASSADOR CONSTR

PAGE 08

01/01/1995 08:00 2129499762

AMBASSADOR CONSTR

PAGE 10

NYC Office Of Emergency Management**Work completion required for Motorola to start Installation****23 Floor:**

- Electrical Riser to Equipment room 11/10/98
- Air-conditioning 11/10/98
- Raised Floor 11/13/98
- Painting 11/13/98
- Room construction 11/13/98

Roof Shelter and Antenna Mounting:

- Approve mounting details for 31 antennas 9/1/98
- Complete I - Beam mounting for antennas 10/15/98 - 10/21
- Grounding for roof area antennas/Shelter 10/15/98 10/20
- Electrical riser to shelter 10/15/98 10/30
- Complete radio room construction 10/15/98 10/20
- Complete Air conditioning 10/30/98 11/15
- Complete Painting 11/1/98 11/15
- Complete Riser for the radio cables to 23 fl 11/1/98 OIC

2 LaFayette - Radio Room & Roof Antenna Mounting:

- Approve mounting details for 19 antennas 10/15/98
- Grounding for roof area antennas 11/15/98
- Grounding for Radio Room 11/15/98
- Electrical riser to shelter 11/15/98
- Complete radio room construction 11/15/98
- Complete Air conditioning 11/15/98
- Complete Painting 11/1/98

Robert B. Hudson 9/28/98

JUL 22 1998 09:49


2129499762

PAGE.10

JUL 25 1998 17:21

2129499762

PAGE.08

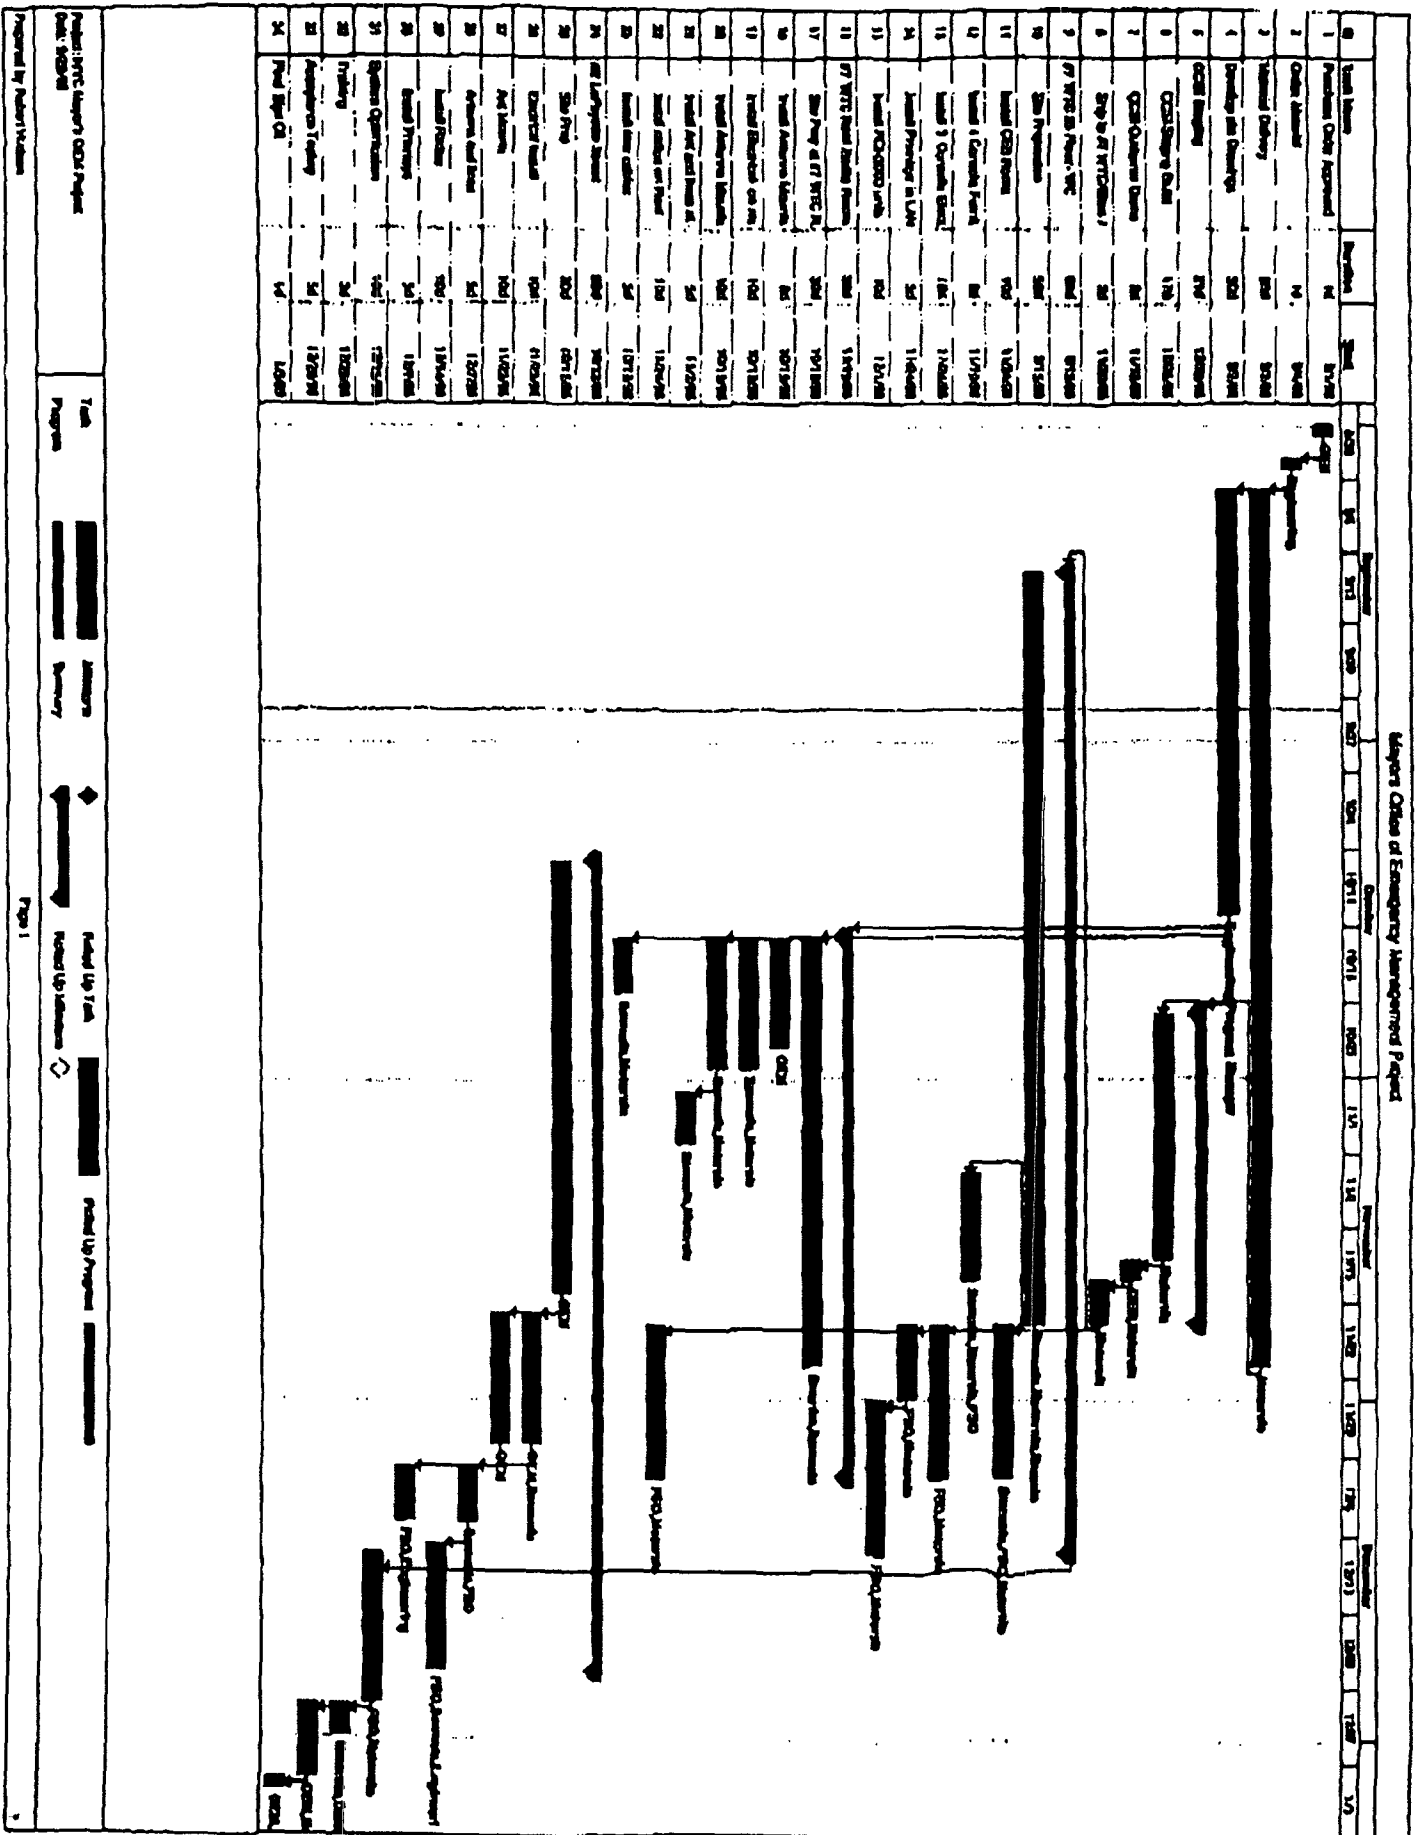

01/03/1995 06:59 2129499762

AMBASSADOR CONSTR

PAGE 10

PROJECT NAME OFFICE OF EMERGENCY MANAGEMENT

SWANKE HAYDEN CONNELL ARCHITECTS

Address 7 World Trade Center
 Address New York, NY 10017
 Project No. 5576A

Date Updated:

10/5
9/21/98**Architectural Sketch Log**

Drawn By	Rev. 1	Rev. 2	Rev. 3	Rev. 4	Rev. 5	Scale	Sheet Size	Remarks
FSK-1	EOC WALL OFFSET	7/22/98				JG	AS NOTED 8 1/2 x 11	
FSK-2	ELEC. OUTLET LOCATIONS RM. # 23-14, 23	8/4/98				JG	1/8"=12'8 1/2 x 11	
FSK-3	P & T DIMENSIONS RM. # 23-13 & 23-15	8/5/98				JG	1/8"=12'8 1/2 x 11	
FSK-3A	ROOM 23-15 MILLWORK AND OUTLET LOC	8/5/98				JG	1/8"=12'8 1/2 x 11	
FSK-4	ROOM 23-02 CEILING DIMENSIONS	8/8/98				JG	1/8"=12'8 1/2 x 11	
FSK-5	ROOM 23-21 PTYE CLARIFICATION	8/12/98				JG	1/8"=12'8 1/2 x 11	
FSK-6	PROTECTIVE WALL DAMPER CONNECTION	8/13/98				JG	1/8"=12'8 1/2 x 11	
FSK-E1	23RD. FLOOR PART PLANS	8/13/98				CA	1/8"=12'8 1/2 x 11	
FSK-E2	ROOF PART PLAN	8/13/98				CA	1/8"=12'8 1/2 x 11	
FSK-E3	LIGHTING PANEL SCHEDULE	8/13/98				CA	1/8"=12'8 1/2 x 11	
FSK-7	P & T LOCATIONS RM. # 23-49 & 23-02	8/17/98				JG	1/8"=12'8 1/2 x 11	
FSK-8	P & T LOCATIONS RM. # 23-04, 23-53	8/17/98				JG	1/8"=12'8 1/2 x 11	
FSK-8	RM. 23-10, PTE CLARIFICATION	8/17/98				JG	1/8"=12'8 1/2 x 11	
FSK-S1	TYP. ANTENNA SUPPORT @ ROOF	8/20/98				AB	NTS 8 1/2 x 11	
FSK-10	RM. 7-01 SWITCHGEAR LOCATION	8/26/98				JG	1/8"=12'8 1/2 x 11	
FSK-11	STEEL FRAME & OVERLY FRAME DETAIL	8/26/98				JG	NTS 8 1/2 x 11	
FSK-12	RM #23-07 OUTLET LOCATION FOR PLASM	9/2/98				JG	1/8"=12'8 1/2 x 11	
SKM-23-1	DELETION OF FSM DAMPERS AROUND LAN	9/2/98				VL	NTS 8 1/2 x 11	
FSK-E4	LIGHTING PANEL SCHEDULE	9/3/98				SG	NTS 8 1/2 x 11	
FSK-13	RM # 23-02 DAMPER & ACCESS PANEL LOC	9/10/98				JG	NTS 11 X 17	
FSK-14	ROOM 23-53, FLOOR BOXES	9/16/98				SK	NTS 8 1/2 x 11	
FSK-15	ROOM 23-23, LAN / HEAD END PTE	9/16/98				JG	NTS 8 1/2 x 11	
FSK-16	RM. # 23-01, 23-40, FINISH CLARIFICATION	9/21/98				JG	NTS 11X17	
FSK-17	PLAN DETAIL @ ENTRANCE DOOR	9/21/98				JG	1 1/2"=11X17	
FSK-18	ELEV. @ ENTRY DR. VIEW CLARIFYING FIN	8/21/98				JG	NTS 11X17	
FSK-19	RM. # 23-40, 23-07, MARLITE CLARIFICATIO	9/21/98				JG	1/4"=12'11X17	

Date Updated:

10/5
9/21/98

[illegible]
