

01/01/1995 05:46 2129499762

AMBASSADOR CONSTR

PAGE 12

01/01/1995 04:21 2129499762

AMBASSADOR CONSTR

PAGE 10

01/03/1995 06:59 2129499762

AMBASSADOR CONSTR

PAGE 08

01/01/1995 08:00 2129499762

AMBASSADOR CONSTR

PAGE 10

NYC Office Of Emergency Management
Work completion required for Motorola to start Installation
23 Floor:

- Electrical Riser to Equipment room 11/10/98
- Air-conditioning 11/10/98
- Raised Floor 11/13/98
- Painting 11/13/98
- Room construction 11/13/98

Roof Shelter and Antenna Mounting:

- Approve mounting details for 31 antennas 9/1/98
- Complete I - Beam mounting for antennas 10/15/98 - 10/21
- Grounding for roof area antennas/Shelter 10/15/98 10/20
- Electrical riser to shelter 10/15/98 10/20
- Complete radio room construction 10/15/98 10/20
- Complete Air conditioning 10/30/98 11/15
- Complete Painting 11/1/98 11/15
- Complete Riser for the radio cables to 23 fl 11/1/98 OK

2 LaFayette - Radio Room & Roof Antenna Mounting:

- Approve mounting details for 19 antennas 10/15/98
- Grounding for roof area antennas 11/15/98
- Grounding for Radio Room 11/15/98
- Electrical riser to shelter 11/15/98
- Complete radio room construction 11/15/98
- Complete Air conditioning 11/15/98
- Complete Painting 11/1/98

Robert B. Hudson 9/28/98

JUL 22 1998 09:49

2129499762

PAGE 10

JUL 25 1998 17:21

2129499762

PAGE 08

OCT 19 1998 13:56

2129499762

PAGE 10

OCT 26 1998 14:02

2129499762

PAGE 12

01/01/1995 05:46 2129499762

AMBASSADOR CONSTR

PAGE 13

01/01/1995 04:21 2129499762

AMBASSADOR CONSTR

PAGE 11

01/03/1995 06:59 2129499762


AMBASSADOR CONSTR

PAGE 09

01/01/1995 00:00 2129499762

AMBASSADOR CONSTR

PAGE 11

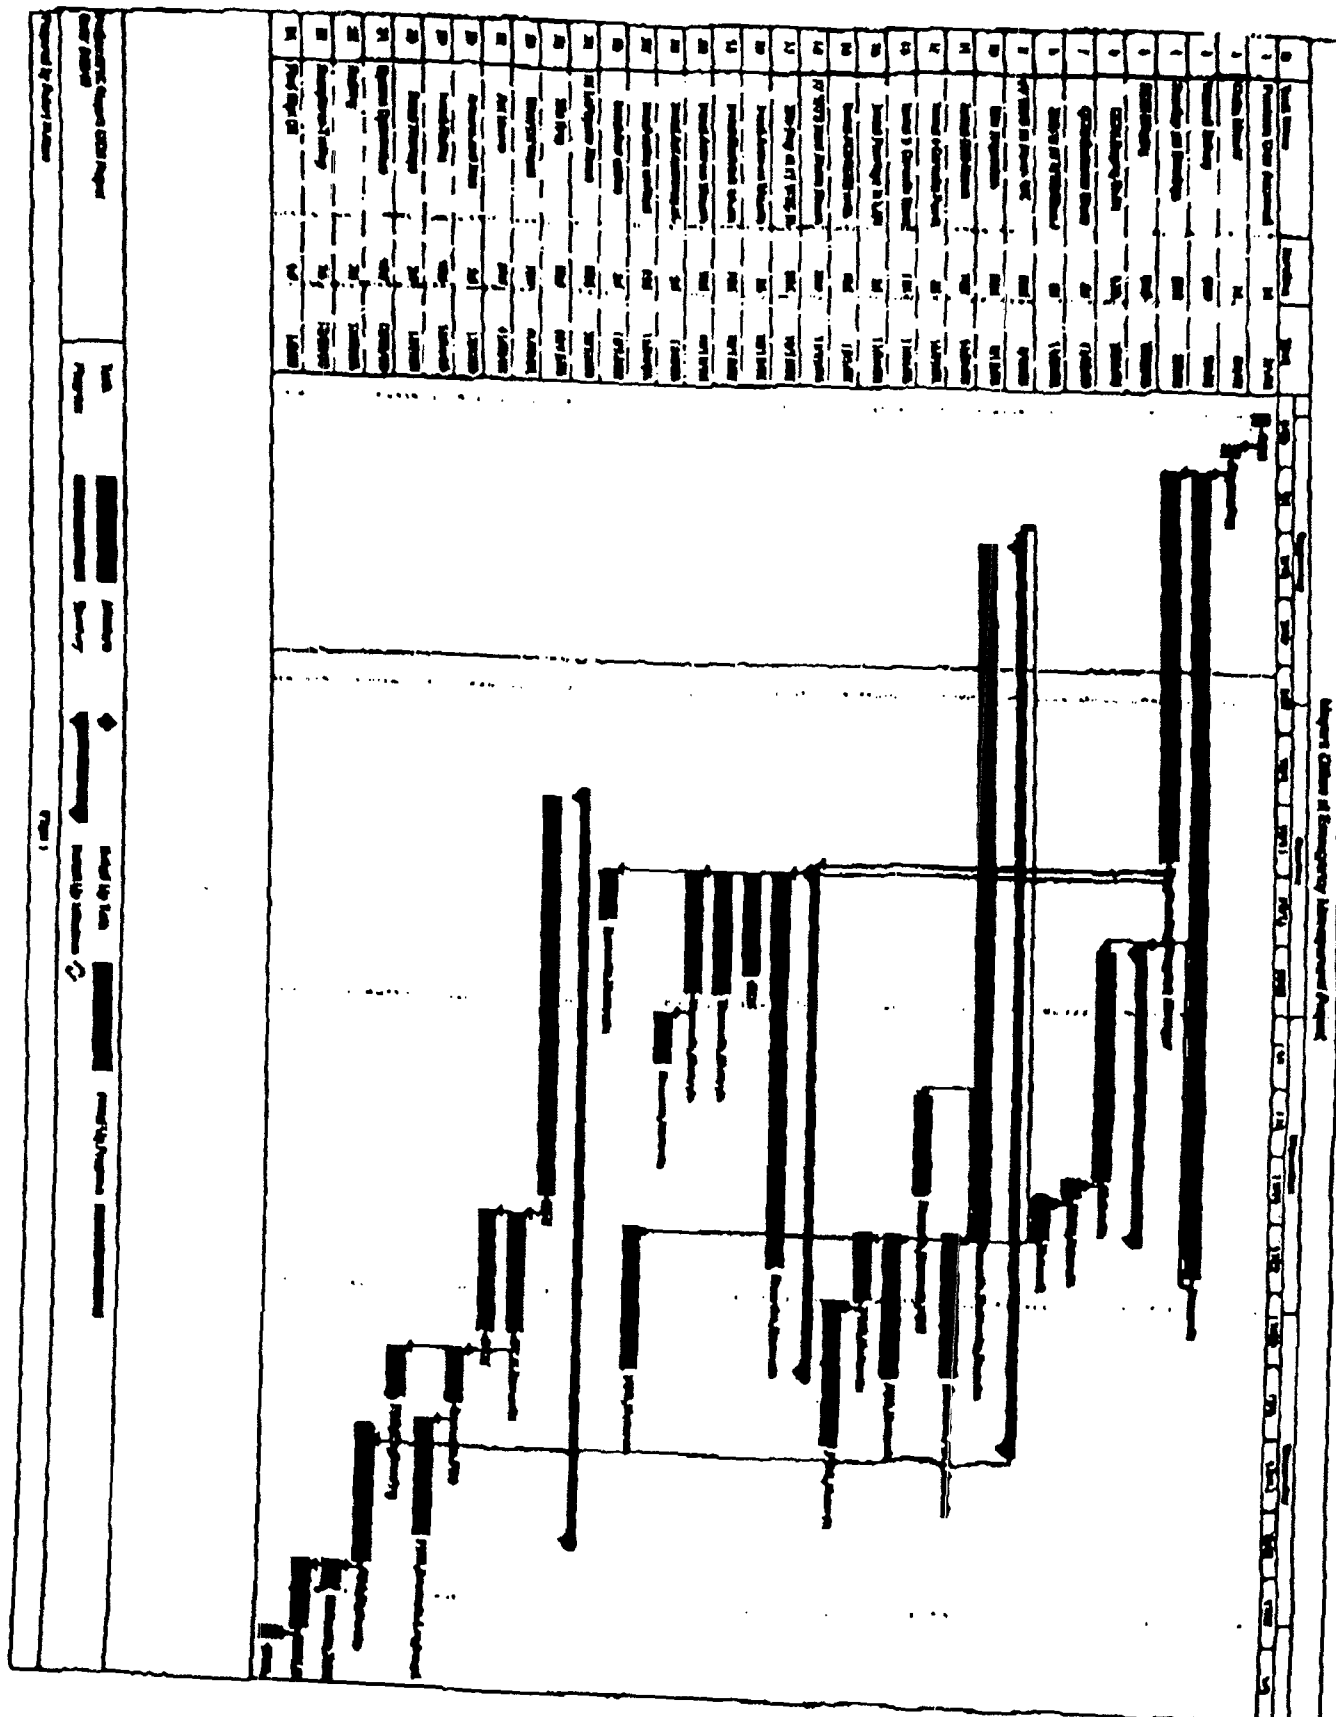

OCT 19 1998 13:56

OCT 26 1998 14:03

NYC-WTC_000173695

2129499762

PAGE.11

2129499762

PAGE.13

01/01/1995 05:46 2129499762

AMBASSADOR CONSTR

PAGE 14

• 01/01/1995 04:21 2129499762

AMBASSADOR CONSTR

PAGE 12

• 01/03/1995 06:59 2129499762

AMBASSADOR CONSTR

PAGE 10

PROJECT NAME OFFICE OF EMERGENCY MANAGEMENT

SWANKE HAYDEN CONNELLY ARCHITECTS

Address 7 World Trade Center
Address New York, NY 10017
Project No. 9576A

Date Updated:

10/6
2009**Architectural Sketch Log**

Sketch No.	Description	Date	Author	Reviewer	Scale	Notes
FSK-1	EOC WALL OFFSET	7/22/98	JG	AS	1/8"=12'	8 1/2 x 11
FSK-2	ELEC. OUTLET LOCATIONS RM. # 23-14, 23-15	8/4/98	JG	1/8"=12'	8 1/2 x 11	
FSK-3	P & T DIMENSIONS RM. # 23-13 & 23-15	8/5/98	JG	1/8"=12'	8 1/2 x 11	
FSK-3A	ROOM 23-15 MILLWORK AND OUTLET LOC	8/5/98	JG	1/8"=12'	8 1/2 x 11	
FSK-4	ROOM 23-02 CEILING DIMENSIONS	8/8/98	JG	1/8"=12'	8 1/2 x 11	
FSK-5	ROOM 23-21 PLYE CLARIFICATION	8/12/98	JG	1/8"=12'	8 1/2 x 11	
FSK-6	PROTECTIVE WALL DAMPER CONNECTION	8/13/98	JG	1/8"=12'	8 1/2 x 11	
FSK-E1	23RD. FLOOR PART PLANS	8/13/98	CA	1/8"=12'	8 1/2 x 11	
FSK-E2	ROOF PART PLAN	8/13/98	CA	1/8"=12'	8 1/2 x 11	
FSK-E3	LIGHTING PANEL SCHEDULE	8/13/98	CA	1/8"=12'	8 1/2 x 11	
FSK-7	P & T LOCATIONS RM. # 23-45 & 23-02	8/17/98	JG	1/8"=12'	8 1/2 x 11	
FSK-8	P & T LOCATIONS RM. # 23-04, 23-53	8/17/98	JG	1/8"=12'	8 1/2 x 11	
FSK-9	RM. 23-10, PTE CLARIFICATION	8/17/98	JG	1/8"=12'	8 1/2 x 11	
FSK-S1	TYP. ANTENNA SUPPORT @ ROOF	8/20/98	AB	NTS	8 1/2 x 11	
FSK-10	RM. 7-01 SWITCHGEAR LOCATION	8/20/98	JG	1/8"=12'	8 1/2 x 11	
FSK-11	STEEL FRAME & OVERLY FRAME DETAIL	8/28/98	JG	NTS	8 1/2 x 11	
FSK-12	RM 823-07 OUTLET LOCATION FOR PLASMA	8/2/98	JG	1/8"=12'	8 1/2 x 11	
FSK-13	DELETION OF FSM DAMPERS AROUND LAN	9/2/98	VL	NTS	8 1/2 x 11	
FSK-14	LIGHTING PANEL SCHEDULE	8/3/98	SG	NTS	8 1/2 x 11	
FSK-15	RM # 23-02 DAMPER & ACCESS PANEL LOC	8/10/98	JG	NTS	11 X 17	
FSK-16	ROOM 23-53, FLOOR BOXES	8/16/98	OK	NTS	8 1/2 x 11	
FSK-17	ROOM 23-23, LAN / HEAD END PTE	8/16/98	JG	NTS	8 1/2 x 11	
FSK-18	RM. # 23-01, 23-40, FINISH CLARIFICATION	8/21/98	JG	NTS	11X17	
FSK-17	PLAN DETAIL @ ENTRANCE DOOR	8/21/98	JG	1 1/2"=1'	11X17	
FSK-18	ELEV. @ ENTRY DR. VIEW CLARIFYING FIN	8/21/98	JG	NTS	11X17	
FSK-19	RM. # 23-40, 23-07, MARLITE CLARIFICATION	8/21/98	JG	1/4"=12'	11X17	

W:\WOOD\Draw\Sketch Log\SKETCH LOG 05M.M

Printed 10/06/09 2:34 PM

Page 1 of 3

JUL 25 1998 17:22

2129499762

PAGE.10

OCT 19 1998 13:57

2129499762

PAGE.12

2129499762

PAGE 14

