NYC 9/11 Public Portal Document

NYC Office Of Emergency Management

Work completion required for Motorola to start Installation

23 Floor:

• Electrical Riser to Equipment room	11/10/98
• Air-conditioning	11/10/98
• Raised Floor	11/13/98
• Painting	11/13/98
• Room construction	11/13/98

Roof Shelter and Antenna Mounting:

• Approve mounting details for 31 antennas	9/1/98	
• Complete I - Beam mounting for antennas	10/15/98	– 10/21
• Grounding for roof area antennas/Shelter	10/15/98	10/30
• Electrical riser to shelter	10/15/98	10/30
• Complete radio room construction	10/15/98	10/20
• Complete Air conditioning	10/30/98	11/15
• Complete Painting	11/1/98	11/15
• Complete Riser for the radio cables to 23 fl	11/1/98	O/C

2 LaFayette - Radio Room & Roof Antenna Mounting:

• Approve mounting details for 19 antennas	10/15/98
• Grounding for roof area antennas	11/15/98
• Grounding for Radio Room	11/15/98
• Electrical riser to shelter	11/15/98
• Complete radio room construction	11/15/98
• Complete Air conditioning	11/15/98
• Complete Painting	11/1/98

Robert B. Hudson 9/28/98

NYC-WTC_000173575

NYC 9/11 Public Portal Document

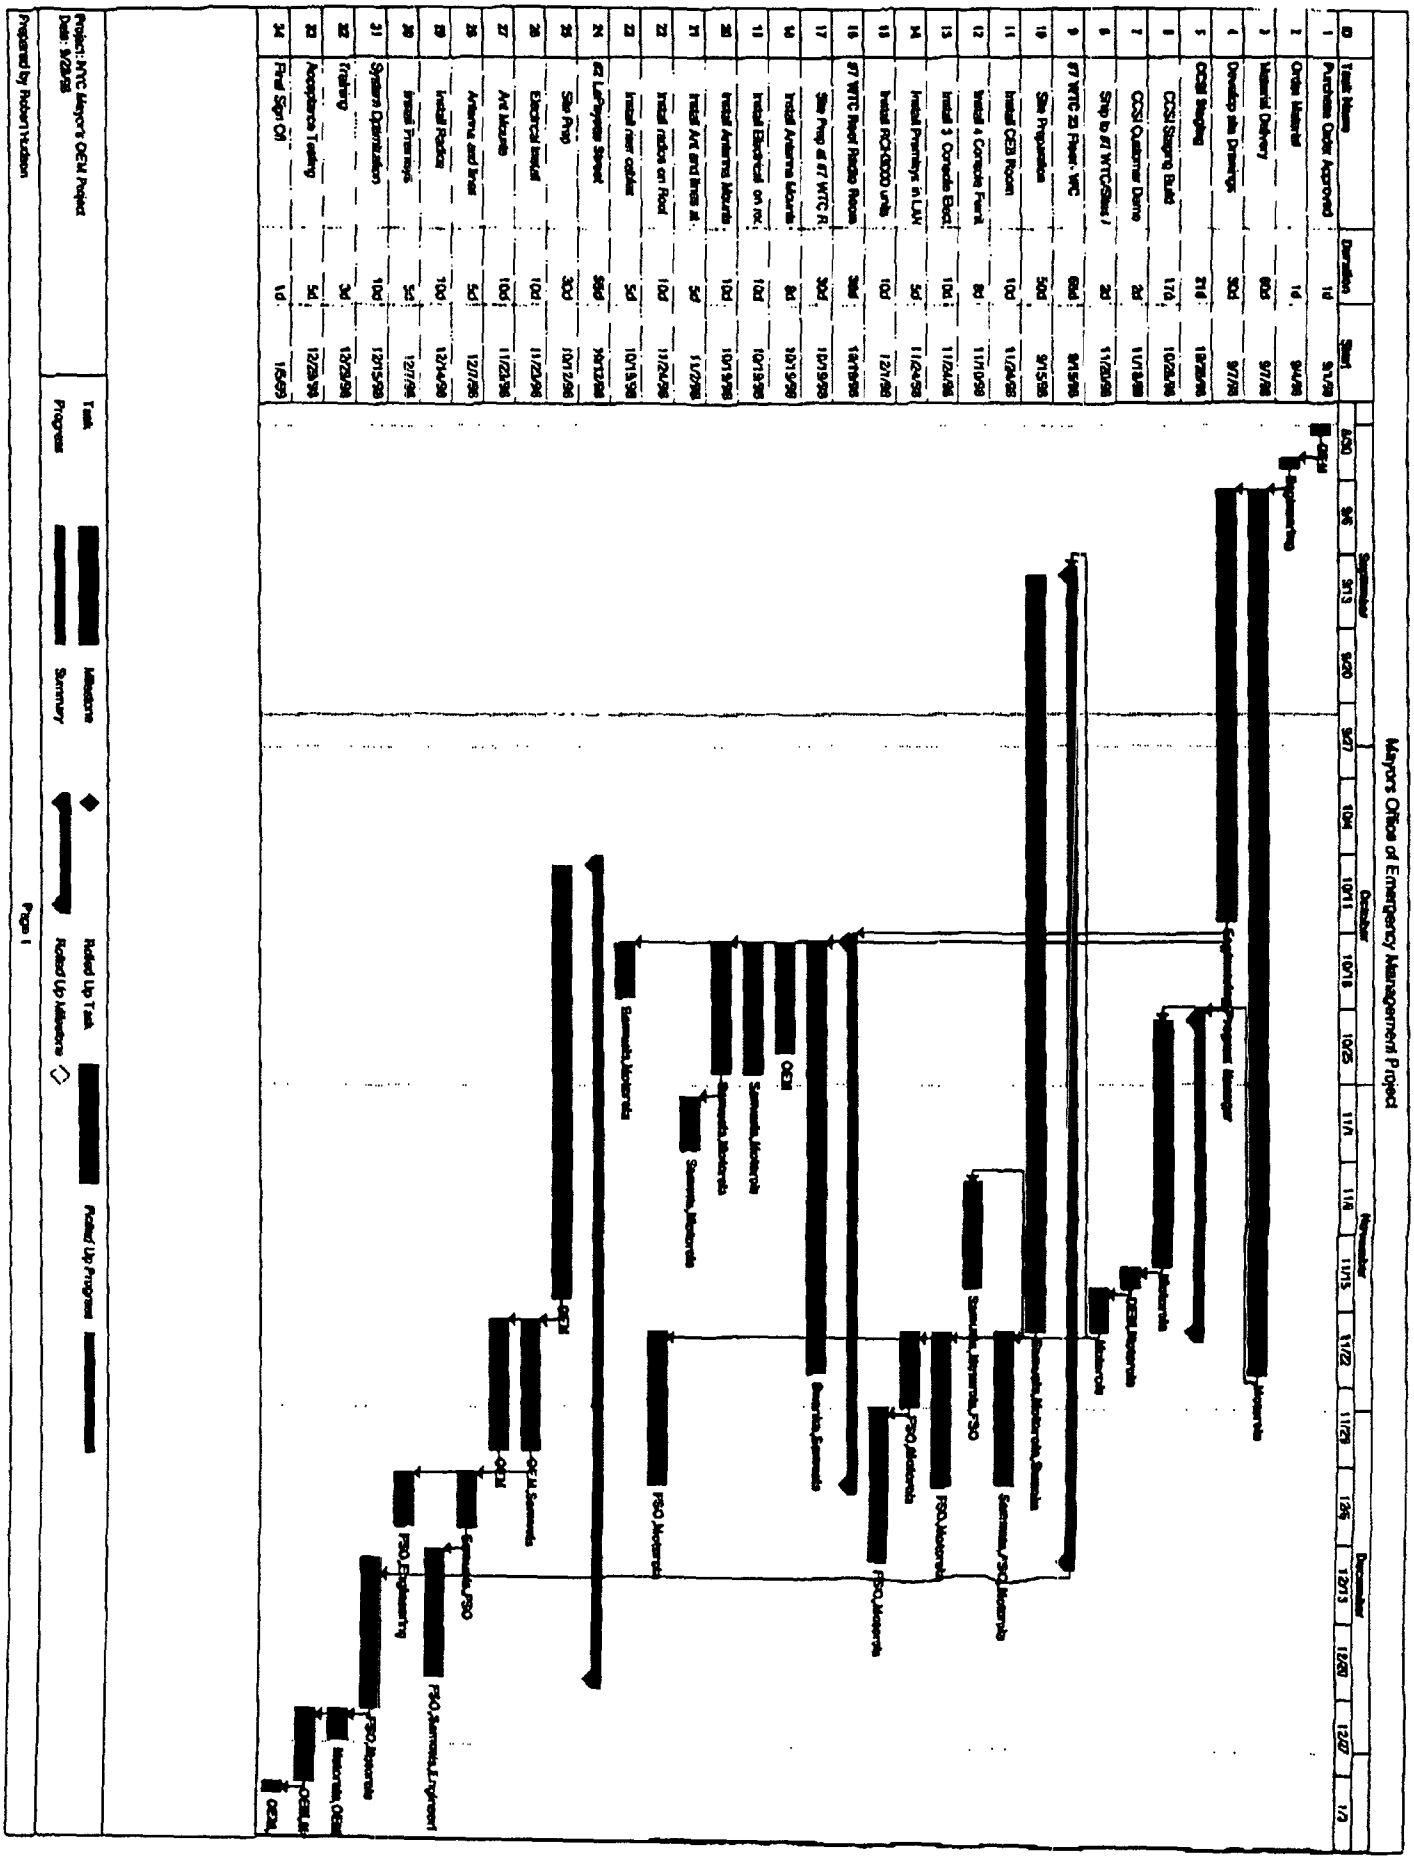

ID	Task Name	Duration	Start
1	Purchase Order Approved	1d	9/1/98
2	Order Material	1d	9/4/98
3	Material Delivery	60d	9/7/98
4	Develop site Drawings	30d	9/7/98
5	OCSI Staging	21d	10/26/98
6	OCSI Staging Build	1.5d	10/26/98
7	OCSI Customer Demo	2d	11/1/98
8	Ship to 81 WTC(Sites)	2d	11/20/98
9	81 WTC 25 Floor - WC	69d	9/15/98
10	Site Preparation	50d	9/15/98
11	Install OEM Room	10d	11/24/98
12	Install 4 Console Fwnt	8d	11/10/98
13	Install 3 Console Back	10d	11/24/98
14	Install Premisys in LAN	5d	11/24/98
15	Install ROHDOO units	10d	12/1/98
16	81 WTC Roof Radio Room	39d	10/19/98
17	Site Prep at 81 WTC R	30d	10/19/98
18	Install Antenna Mounts	8d	10/19/98
19	Install Electrical on rac	10d	10/19/98
20	Install Antenna Mounts	10d	10/19/98
21	Install Ant and lines at	5d	11/2/98
22	Install radios on Roof	10d	11/24/98
23	Install riser cables	5d	10/19/98
24	81 LaPlayette Street	56d	10/13/98
25	Site Prep	30d	10/13/98
26	Electrical Install	10d	11/20/98
27	Ant Mounts	10d	11/23/98
28	Antenna and lines	5d	12/7/98
29	Install Radios	10d	12/14/98
30	Install Premisys	5d	12/7/98
31	System Optimization	10d	12/15/98
32	Training	3d	12/29/98
33	Acceptance Testing	5d	12/29/98
34	Final Sign Off	1d	1/5/99

NYC-WTC_000173576
